

Resident maintenance service integration

Evidence-based recommendation for client decision

Final decision presentation

Prepared by Kylie Bi | May 2027

Controlled staged expansion is the strongest next step

RECOMMENDATION

Continue the current operating model and expand in controlled phases.

The Core architecture remains suitable. The next phase should test operating capacity and contractor readiness before any portfolio-wide rollout.

WHY THIS PATH

- 01 Measured service gains**
Response, transfer, creation and repeat-contact measures improved materially.
- 02 Architecture held**
No critical integration incident, rollback or identified silent creation failure occurred.
- 03 Remaining issues are controllable**
Contractor practices, capacity, policy and commercial readiness can be managed through explicit gates.

This recommendation does not authorise portfolio-wide rollout. Each phase remains subject to the client's governance gates.

The pilot provides a strong operational signal within a defined boundary

8 weeks

Live pilot period

22 February to 18 April 2027

418

Homes

574

New maintenance events

521 approved formal work-order cases

5

Intake routes

2

Approved sites


EVIDENCE BOUNDARIES

- Results apply to the approved cohort and participating contractors.
- Contractor-group sample counts were not provided; comparisons are directional.
- No comparable pre-pilot staff-time baseline was available.
- Expansion and renewal prices remain unconfirmed.

OUTSIDE PILOT SCOPE

AI assistant and field extraction
WhatsApp expansion
Gamma screen-pop
Passwordless upload

The pilot improved speed and reduced manual handling

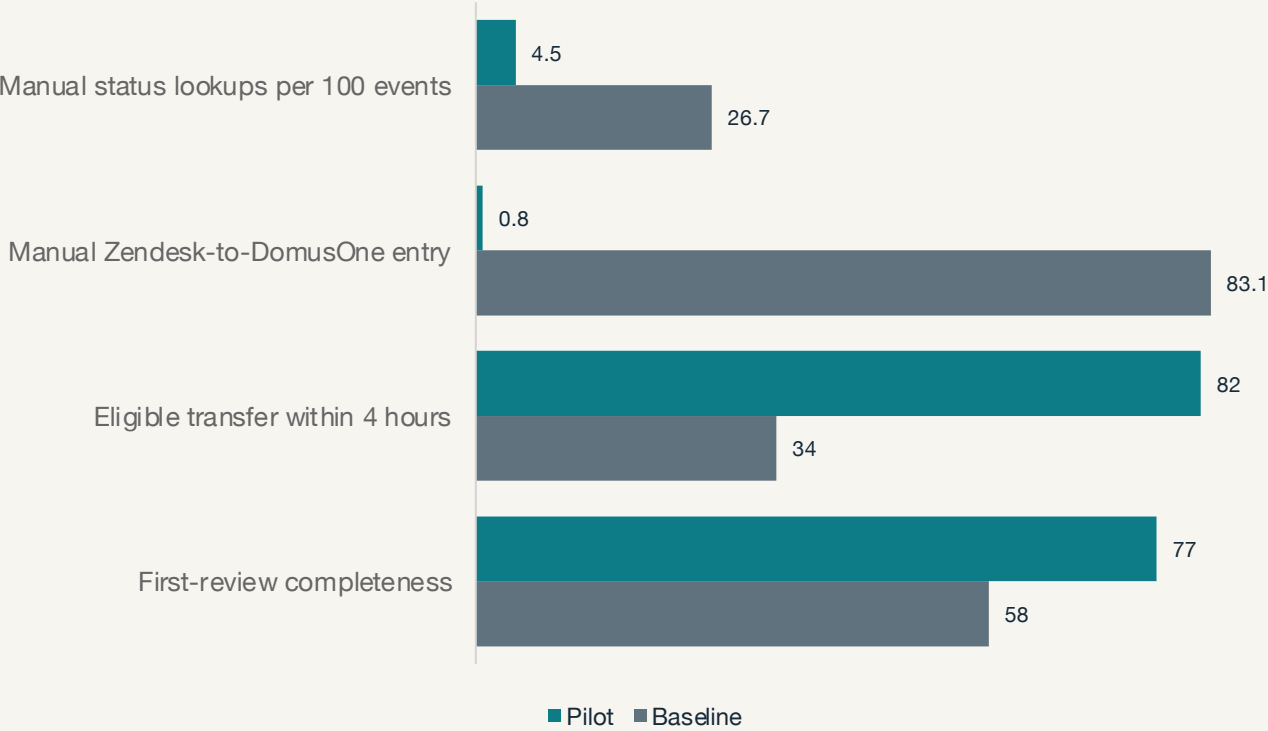

MEAN MEANINGFUL FIRST RESPONSE

3.6 → 1.2 **–66.7%**
working days

MEDIAN TIME FROM COMPLETENESS TO CREATION

6.4 → 1.7 **–73.4%**
working hours

Note: the chart combines percentages and event rates to compare direction of change; labels preserve the original units.

Two provisional targets were not achieved, despite material gains from baseline

MEAN MEANINGFUL FIRST RESPONSE

1.2 working days

Target: below 1.0 working day

The mean missed the provisional target by 0.2 working days.
The median was 0.6 working days.

FIRST-REVIEW COMPLETENESS

77%

Target: 85%

Completeness improved by 19 percentage points from the 58% baseline. Incomplete or ambiguous submissions still required manual clarification before transfer.

Implication

Keep both measures as next-stage operational priorities; do not treat either as an architecture failure.

The integration handled pilot production volume without critical incidents or data loss

521

Approved formal work-order cases

508 first-pass, 9 controlled retry, 4 continuity procedure

100%

Final creation

Across all approved cases

0

Critical integration incidents

0

Identified silent creation failures

47-minute longest middleware interruption

Event-history recovery completed successfully without data loss.

20 vendor support tickets

14 implementation-partner tickets and 6 supplier tickets. Support records are suitable for service-performance assessment, not transaction-level root-cause analysis.

Expansion readiness varies with contractor update practices

Metric	Large portal contractor	Smaller contractors
Same-day status updates	93%	49–62%
Structured appointment use	95%	67–78%
Status correction required	4%	17–24%
Progress contacts generated	11%	19–24%

Interpretation

Structured status and appointment updates produced the strongest results. Future cohort selection should include contractor-readiness criteria and agreed update standards.

Evidence limit: group-level sample counts were not provided. Compare directionally rather than as a statistically weighted portfolio estimate.

Two policies require client approval before expansion

COMPLETED COMMUNICATION

9 of 403 Completed messages were disputed

2.2% observed dispute rate

Recommended policy

Retain automatic notification, revise the resident-facing wording, and introduce staff confirmation only for agreed higher-risk repair categories.

REPEATED OUT-OF-HOURS CALLS


11 groups of repeat calls created separate tickets

Recommended policy

Retain separate auditable tickets linked by a stable incident reference. Do not introduce an alternative consolidation rule until it has been designed and tested separately.

Both recommendations remain subject to formal client policy approval.

Current commitments remain below the first-year planning ceiling

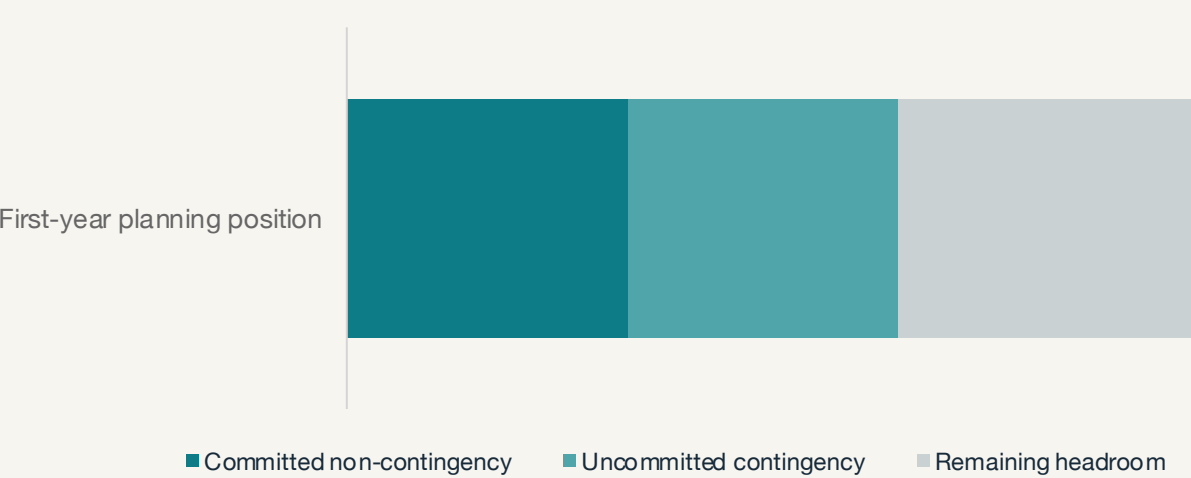

€52,000 committed | €3,840 reserve | €4,160 headroom

€55,840

first-year planning position, including reserve

RENEWAL AND EXPANSION GATES

Nov 2027	DomusOne Connector
Dec 2027	Hosted middleware
Feb 2028	SMS service and Zendesk
Jun 2028	DomusOne platform

Expansion and renewal prices are not fixed. The €4,160 headroom is not an approved expansion budget.

AI is not required for the next stage

The pilot demonstrated substantial improvement without AI assistance or AI field extraction.

The immediate priority is to stabilise and expand the current operating model under controlled conditions.

SEPARATE AI DECISION GATE

- Evidence of an unresolved service gap and a defined use case
- Identified product, licence and processing model
- Confirmed data locations, processor terms and access controls
- Defined human-review model, cost and success measures
- IT, Digital Services and Procurement assessment
- Independent DPO review and DPIA position
- Separate Sponsor authorisation and residual-risk acceptance
- No assumption that future approval will be granted

Other deferred components: WhatsApp expansion, Gamma screen-pop and passwordless upload.

Four paths were assessed against evidence, readiness and risk

Option	Benefit	Key limitation	Assessment
1 Stop and revert	Lowest change exposure	Abandons measured gains and existing investment	Not recommended
2 Continue current cohort	Allows further operational refinement	Does not test scale or spread benefits	Viable short hold
3 Controlled staged expansion	Extends benefits while testing readiness and capacity	Requires explicit gates and monitoring	Recommended
4 Immediate broad rollout	Fastest portfolio coverage	Capacity, contractor quality, support and costs remain unconfirmed	Not recommended now

Recommendation condition

Proceed only after contractor readiness, operating capacity, policy, commercial, data-protection and phase-specific risk gates are satisfied.

Expansion should proceed only with named controls and owners

Residual risk	Current control	Required next-stage action
Late or unstructured contractor updates	Pilot monitoring and manual follow-up	Apply contractor-readiness criteria before each phase
Completed message may imply verified finality	Resident review and follow-up	Approve wording and targeted confirmation policy
Repeated OOH calls create separate tickets	Stable incident reference and manual linking	Approve retained-ticket policy or test an alternative separately
Operating effort may not scale predictably	Pilot hours and exception volumes recorded	Measure BAU capacity during every phase
Integration interruption delays events	Monitoring, retry and history recovery	Confirm scaled support and recovery objectives
Renewal and expansion prices are not fixed	Renewal schedule available	Obtain costed renewal and expansion position
AI or new channels create new data risk	Explicitly deferred	Require a separate evidence and authorisation gate

Decision gates for controlled expansion

Gate	Decision or evidence	Principal owner
1 Strategic direction	Select the next planning path	Executive Sponsor
2 Cohort and contractor readiness	Approve homes, channels, contractors and capacity	Resident Services + Maintenance Operations
3 Operating policies	Approve Completed communication and repeated OOH-call policies	Resident Services + OOH Contract Manager
4 Support and capacity	Confirm operating capacity, support and recovery objectives	IT + service owners
5 Commercial readiness	Approve renewal and expansion envelope	Finance + Procurement
6 Data protection and security	Confirm processing design and independent DPO position	Business/data owner + IT; DPO review
7 Phase go-live and risk acceptance	Accept residual business risk and authorise the phase	Executive Sponsor or authorised controller representative
8 Phase review	Continue, hold or revise after evidence review	Executive Sponsor + service owners

Decisions for client consideration at the meeting

These decisions authorise the next-stage planning path. They do not authorise portfolio-wide rollout or later phase go-live.

1	Confirm strategic direction	Select controlled staged expansion as the planning direction.
2	Authorise next-cohort planning	Ask Resident Services and Maintenance Operations to propose the next cohort against readiness and capacity criteria.
3	Authorise commercial and support assessment	Obtain renewal and expansion quotations and confirm scaled support requirements.
4	Confirm the AI and optional-component position	Defer these components to separate evidence, governance and authorisation gates.
5	Confirm the governance sequence	Require every expansion phase to pass the named operational, commercial, data-protection, risk and go-live gates.

The Project Lead or Executive Sponsor chairs the meeting and maintains the formal decision record. The adviser presents findings and responds to questions.
